

# 2

## Library & Student Resource Center Campus Master Plan Project



Western University  
OF HEALTH SCIENCES


### ACTIVE PROJECT

This project will create new student study space, relocate LEAD to the 1<sup>st</sup> floor, establish a "wellness" space for students and relocate some of the library staff.

#### Summary:

- Renovations include:
  - 1<sup>st</sup> FL, 6,742 sq. ft.
  - 2<sup>nd</sup> FL, 7,080 sq. ft.
  - 3<sup>rd</sup> FL, 7,080 sq. ft.
  - 4<sup>th</sup> FL, 7,080 sq. ft.
  - Basement 5,740 sq. ft.
- Student, staff & faculty library survey sent on April 2019
- Survey results compiled in June 2019
- Partial Funding Approved: November 2018
- Project Start Date: April 2019
- Anticipated Construction Start Date: April 2020
- Anticipated Completion Date: September 2021

LEAD  
(Director Office)

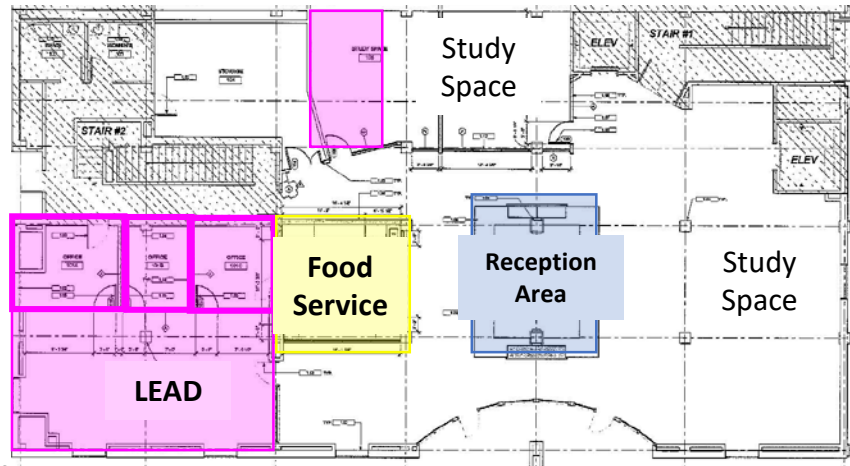


#### First Floor:

LEAD office and staff will be relocated to the first floor of the Library Resource Center. A food service space will be created in the first floor as well as open student study space.

#### Project Status:

#### Funding Status:



Design and Approval



Project Partially  
Funded

- Total Project Cost: \$2,194,000
- Total Approved: \$449,000
